

Private Cloud Modernization



Seven Modernization Scenarios. One Unified TPM Delivery Model.

Dashboard

Plan

Delivery

Governance

Closure

danvzla.github.io/private-cloud-modernization-tpm

Daniel Mazzini - Principal Architect & Senior TPM

Independent portfolio demo - illustrative, non-client data

Modernization programs stall before execution


Technical complexity is not the only issue. Program clarity is the bottleneck.

Week 0	Unclear starting state	Architect / TPM
Week 1	No integrated roadmap	Senior TPM
Week 2	Risks and dependencies hidden	Workstream Leads
Week 3	Jira work not tied to outcomes	Delivery Teams
Week 4	Executive reporting lacks decisions	Program Sponsor
After cutover	Closure and benefits tracking missed	Operations Owner

Result: programs look busy, but leaders cannot see readiness, risk, decisions, or value.

Seven illustrative modernization paths, one TPM control model


Each scenario has different risk, schedule, governance intensity, and delivery rhythm.

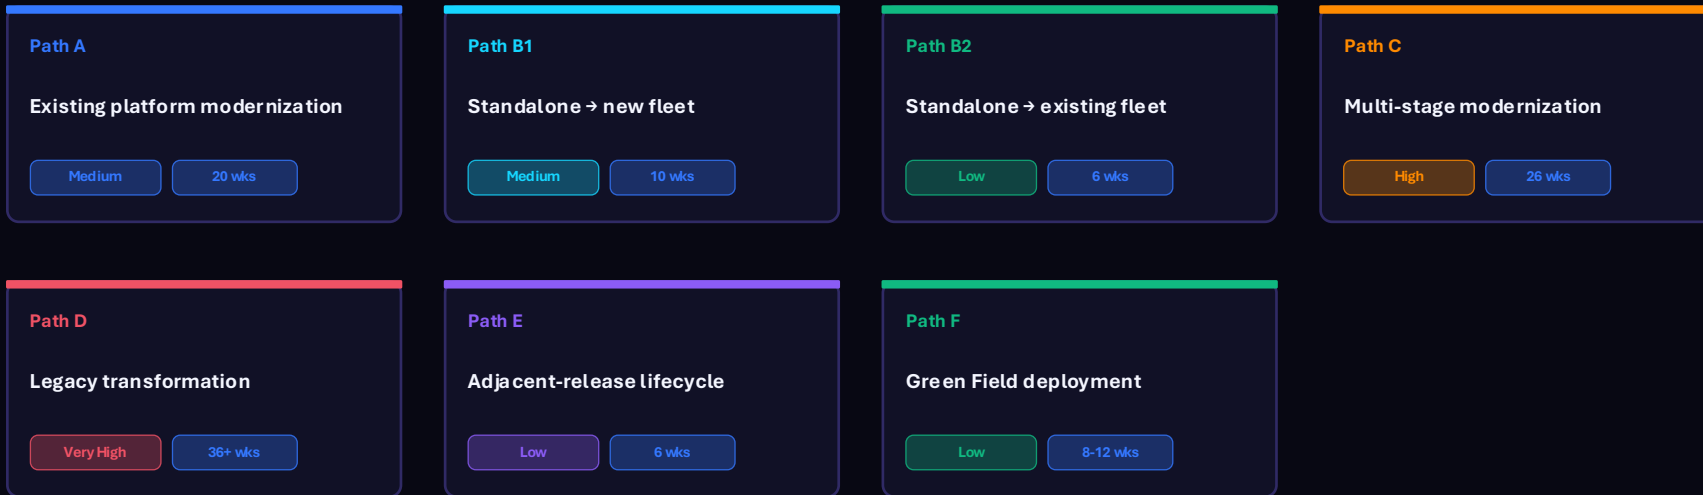

The value is not the path list. It is the repeatable TPM operating model applied consistently across all scenarios.

Five views that map executive control to delivery execution


Dashboard · Plan · Delivery · Governance · Closure

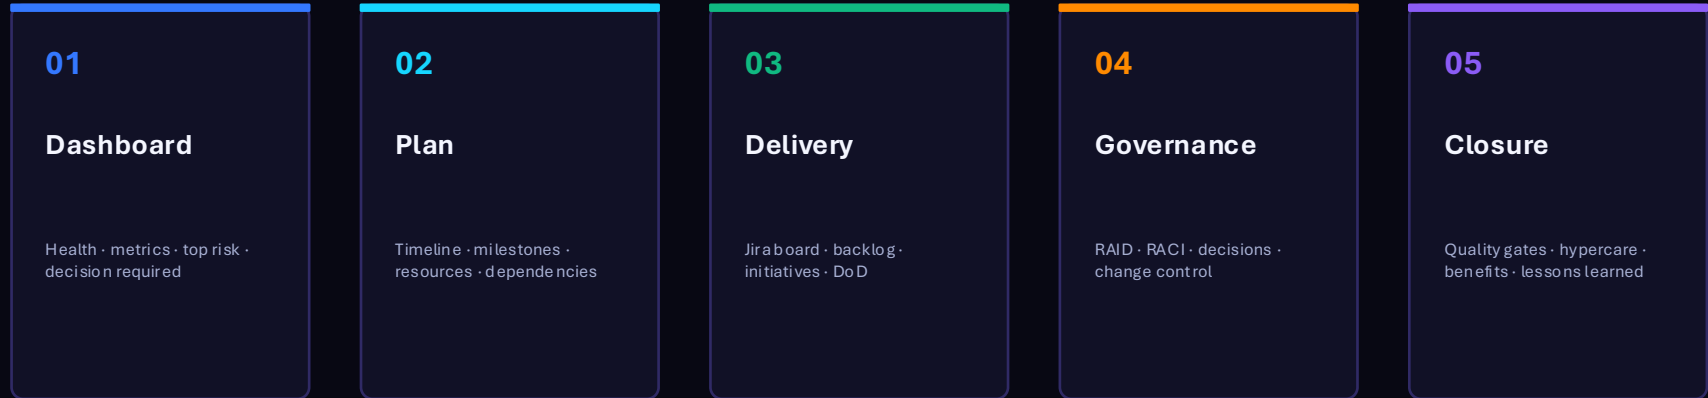

Understand → Plan → Execute → Control → Close


Decision-ready executive status at the top

The first screen answers what leaders need to know before opening the details.

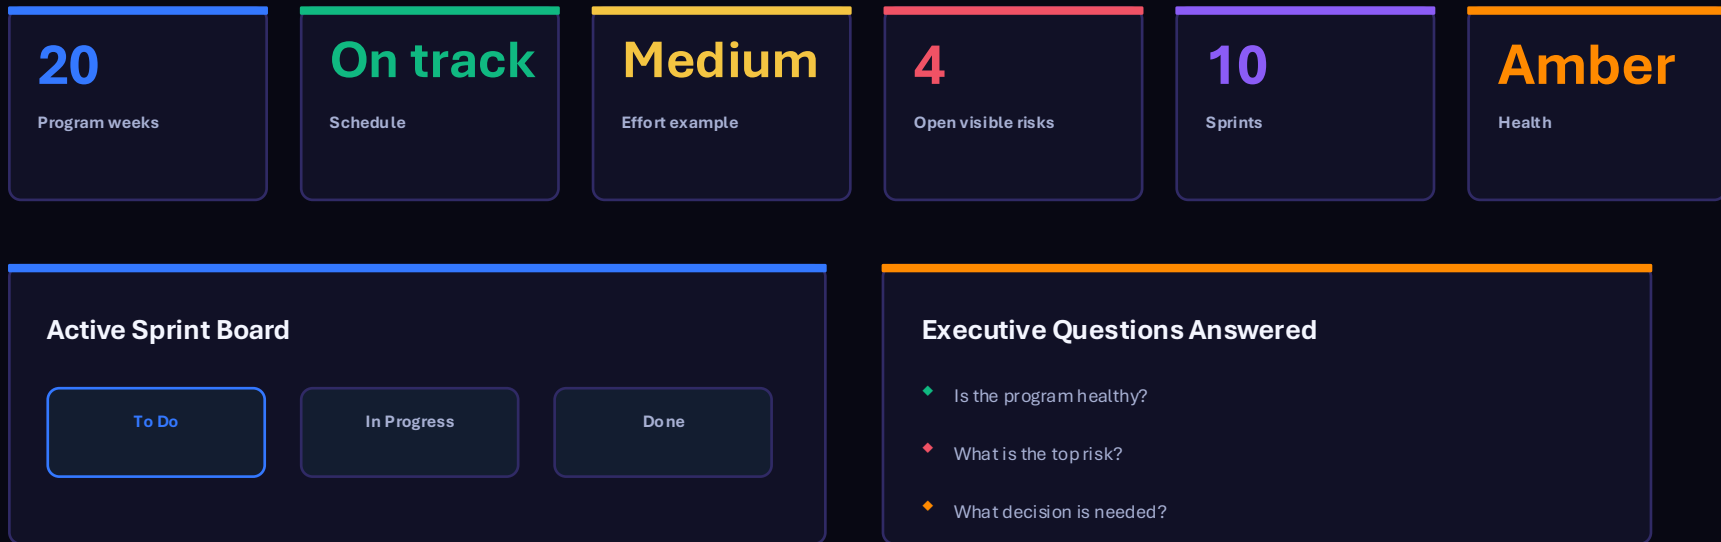


Timeline, milestones, resources, and dependencies in one view

A program plan is more than a Gantt chart. It is a decision and readiness system.

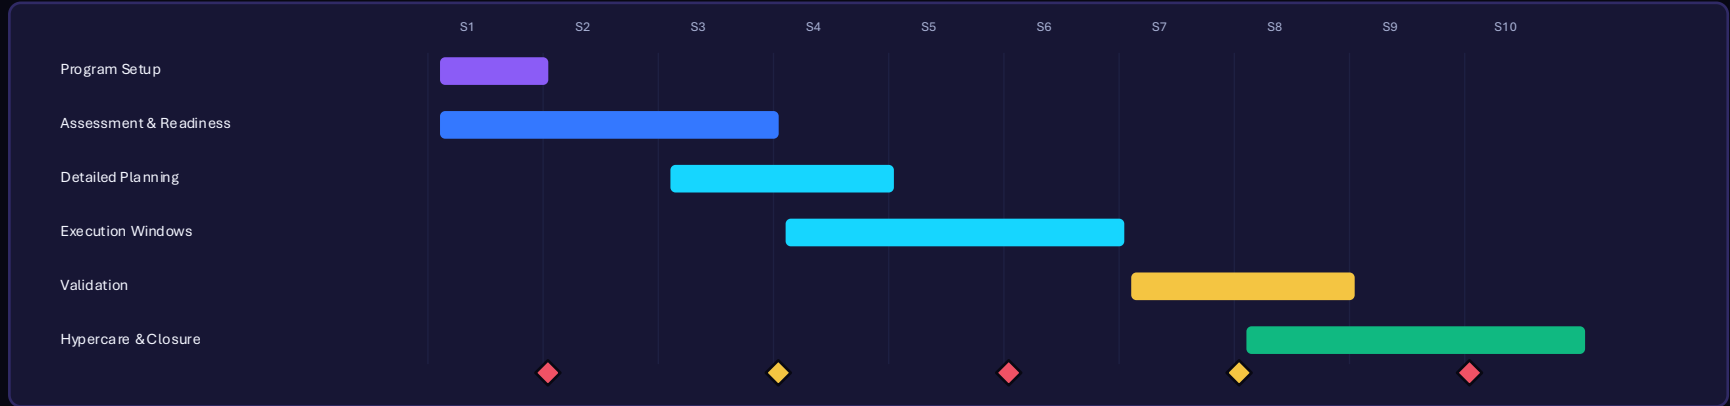

From business outcome to active sprint board

Jira execution becomes credible only when work traces back to outcomes.

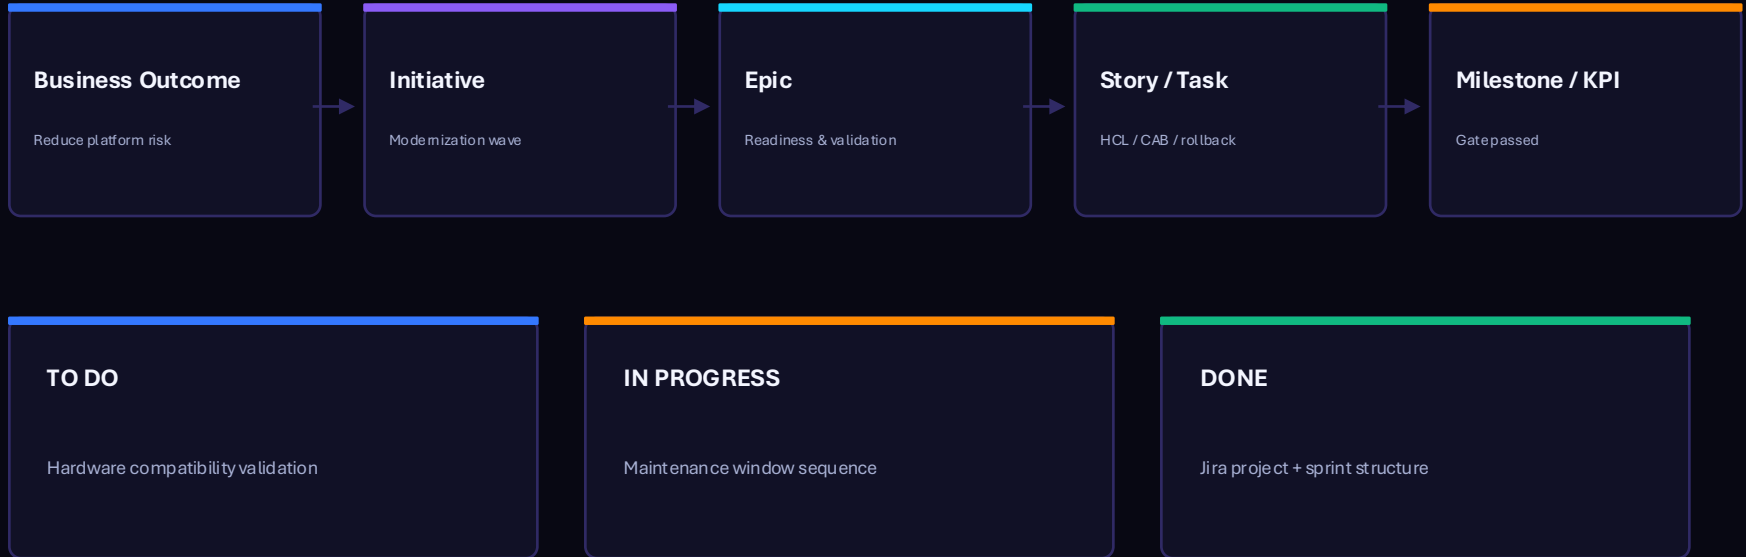

RAID, RACI, decisions, changes, and communication cadence

The demo makes accountability visible before issues become escalations.

RAID Register

Risks · assumptions · issues · dependencies

RACI Matrix

Sponsor · TPM · architect · domain leads · operations

Decisions & Changes

DEC and CR logs tied to owners and status

Communications

Daily · weekly · executive · CAB · post-window

Path A includes a detailed technical RACI and expanded governance register to demonstrate program depth.

Reports a TPM can use during real program calls

Six downloads convert the portfolio from a demo into an operating model.

Executive Status Report

Decision-ready HTML / Save as PDF

Daily Program Call Brief

Blockers · actions · active sprint

Weekly Program Status

RAG · milestones · risks · asks

RAID Log

CSV export for governance review

Milestone Plan

CSV with acceptance criteria

Jira Backlog

CSV with epics, stories, tasks

Every export includes the independent portfolio disclaimer and reflects the selected program path.

Static, browser-native, self-contained portfolio

No backend. No database. One HTML app plus structured program data.

PRESENTATION

index.html · responsive UI · executive/detailed views · search · exports

PROGRAM DATA

Seven scenarios · metrics · boards · RAID · RACI · milestones · reports

INTERACTION

Path selector · tabs · active board · report generation · CSV download

Designed as a portfolio artifact: lightweight, portable, and safe to share publicly with illustrative, non-client data.

Program timeline and milestone controls in the live demo

Path A dashboard view shown with metrics, timeline, milestones, and active program controls.



What this demonstrates — and what it replaces

A focused TPM portfolio artifact for recruiters, hiring managers, and interview teams.

7

Scenarios

Private cloud modernization contexts

5

Views

Dashboard, Plan, Delivery, Governance, Closure

6

Exports

Reports and CSV artifacts

0

Client data

Illustrative portfolio content only

1

Operating model

Consistent TPM control system

∞

Interview use

Walkthroughs, examples, discussion prompts

Try it right now



[Live demo → danvzla.github.io/private-cloud-modernization-tpm](https://danvzla.github.io/private-cloud-modernization-tpm)

[GitHub → github.com/danvzla/private-cloud-modernization-tpm](https://github.com/danvzla/private-cloud-modernization-tpm)

- ◆ Start Here → review purpose and disclaimer
- ◆ Discovery → compare seven illustrative scenarios
- ◆ Programs → switch Executive / Detailed views
- ◆ Exports → generate executive, daily, weekly, RAID, milestone, and backlog artifacts

Daniel Mazzini

Principal Architect & Senior TPM · Cloud & Infrastructure · Telco · Applied AI
